Appendix 1 Consultation Letter

(Total No. of pages including blank pages = 24)





29 November 2022

Name	Sent by email to:
Company	
Address 1	
Address 2	
Attention:	
Dear	

Re: North East Copper Mine Rehabilitation Management Plan: Draft Rehabilitation Objectives and Completion Criteria

Tritton Resources Pty Limited (the "Company"), a wholly owned subsidiary of Aeris Resources Limited, owns and operates the North East Copper Mine (the "Mine"). The Mine is located approximately 3.5km west of the Girilambone, and 45km northwest of Nyngan and operates under Development Application (DA) 1/91 and Mining Lease (ML) 1280 (the "Mine Site") (see **Attachment A**).

Long-term mine closure principles and rehabilitation activities for the site are currently detailed in the approved Mining Operations Plans (MOPs) which, following recent changes to the *Mining Act 1992* have ceased to have effect. In order to detail progressive rehabilitation operations, rehabilitation objectives and proposed final land uses, the Company is currently preparing a Rehabilitation Management Plan (RMP) for the Mine. Tritton has commissioned R.W. Corkery & Co. Pty Limited (RWC) to assist with the preparation of the RMP.

The RMP is being prepared in accordance with the following documents and guidelines.

- Form and Way: Rehabilitation Management Plan for Large Mines (July 2021).
- Form and Way: Rehabilitation Objectives, Rehabilitation Completion Criteria and Final Landform and Rehabilitation Plan for Large Mines (July 2021).
- Guideline 1: Rehabilitation Risk Assessment (July 2021).
- Guideline 2: Rehabilitation Records (July 2021).
- Guideline 3: Rehabilitation Controls (July 2021).
- Guideline 5: Rehabilitation Objectives and Rehabilitation Completion Criteria (July 2021).

In accordance with Section 4.2 of the *Form and Way: Rehabilitation Management Plan for Large Mines* guideline document, consultation with relevant stakeholders must be undertaken during the preparation of the rehabilitation objectives and rehabilitation completion criteria for the Mine. Rehabilitation objectives describe the rehabilitation outcomes required to attain the final land use for the mining area. Rehabilitation completion criteria define the key criteria which, once attained, will demonstrate that rehabilitation has been achieved. The following subheadings address the requirements for consultation.

ABN: 31 002 033 712 Telephone: (02) 9985 8511 Email: admin@rwcorkery.com

Final Land Use

Condition 2 of the development consent for the Mine (DA 6/95) states that development is to be undertaken in accordance with the *Environmental Impact Assessment* (EIS) that was submitted in 1995 (RWC, 1995). A final land use options assessment is not required as Section 2.11 of the EIS describes the intended land use as a combination of productive grazing and native vegetation establishment.

Attachment B provides a copy of the draft Final Landform Features (Plan 1) prepared for the Mine Site for your information. It is expected that most rehabilitated areas of the Mine Site would be suitable for grazing with native vegetation establishment to support this consistent with the surrounding land uses.

The approved final land use goals for the North East Mine are as follows.

- To provide a low maintenance, stable and safe landform commensurate with grazing land use capability.
- To revegetate with native tree and shrub species comparable with pre-existing vegetation communities.
- To provide a stable ground cover for erosion control.

These land use goals have been clearly established from the commencement of operations and are not expected to change.

As the final land use has already been defined in the aforementioned documents no further comments are needed from stakeholders at this time. However, the Company would welcome informal feedback on this matter.

Rehabilitation Objectives and Completion Criteria

The proposed rehabilitation objectives and rehabilitation completion criteria, presented in **Attachment C**, apply to the final land use domain areas, presented in **Table A** and **Attachment B**, for the Quarry Site (see **Attachment B**).

Table A
Final Land Use Domains

Plan 1				
Domain ID Final Land Use Domain				
В	Agricultural – Grazing			
G	Water Management Area			
I	Infrastructure Area			
J	Final Void			

Each final land use domain is presented in **Attachment C** with the table detailing.

- The phases of rehabilitation from decommissioning to relinquishment.
- The rehabilitation objectives for each domain and phase of rehabilitation.
- The performance indicators for each domain and phase of rehabilitation that will provide and progressive indication of success or the need for remedial action.

• The completion criteria for each domain and phase of rehabilitation that will be satisfied in order for rehabilitation to be considered complete.

• The validation method for each domain and phase of rehabilitation so that the Company can demonstrate satisfaction of the completion criteria.

The Company is seeking feedback on the rehabilitation objectives and rehabilitation completion criteria presented in **Attachment C**. Consultation on these matters is a requirement of the *Form and Way: Rehabilitation Management Plan for Large Mines* guideline document. Nonetheless, the Company welcomes feedback on all aspect of its rehabilitation planning.

It is the Company's intention to finalise the draft RMP for the Mine Site as required by the NSW Resources Regulator in coming weeks. We therefore request that you provide any feedback in relation to the rehabilitation objectives and rehabilitation completion criteria as soon as practical.

If you have any questions or concerns, please do not hesitate to contact myself (<u>nick@rwcorkery.com</u>) or Mr Quinton Bruwer, Environmental Superintendent at the Mine Site (<u>qbruwer@aerisresources.com.au</u>).

Yours sincerely

Nick Warren

Principal Environmental Consultant

 $Encls: \ \ Attachment \ A-Figure \ 1-Locality \ Plan.$

Attachment B – Final Landform Features.


Attachment C – Rehabilitation Objectives and Rehabilitation Completion Criteria Table.

Copy: Tritton Resources

Attachment A

Figure 1 - Locality Plan


(Total No. of pages including blank pages = 2)

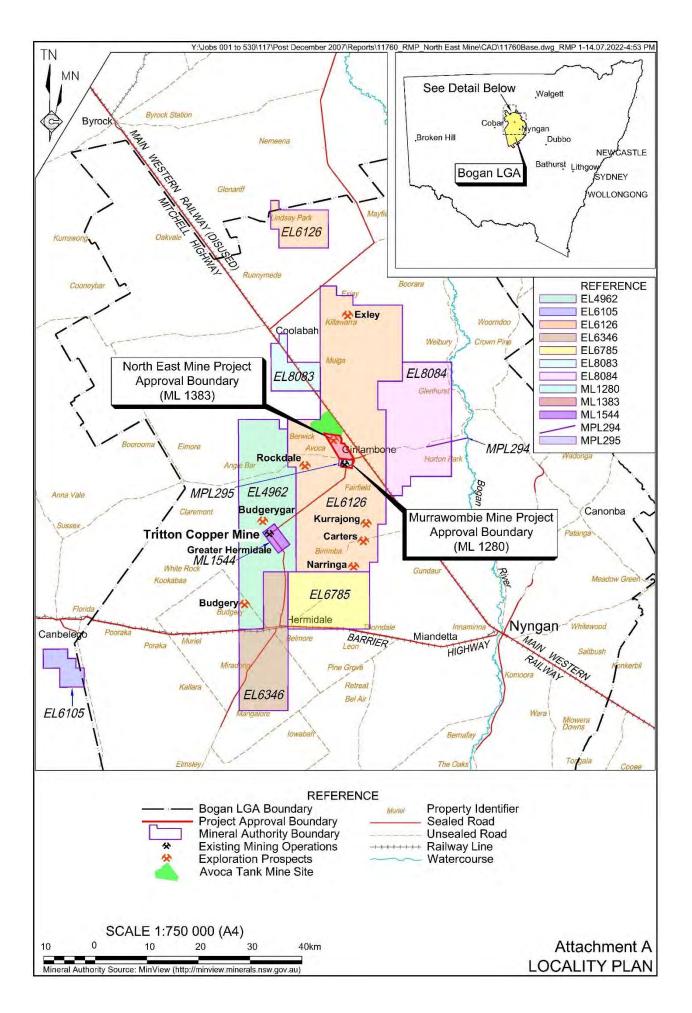

Attachment B

Final Landform Features

(Total No. of pages including blank pages = 2)

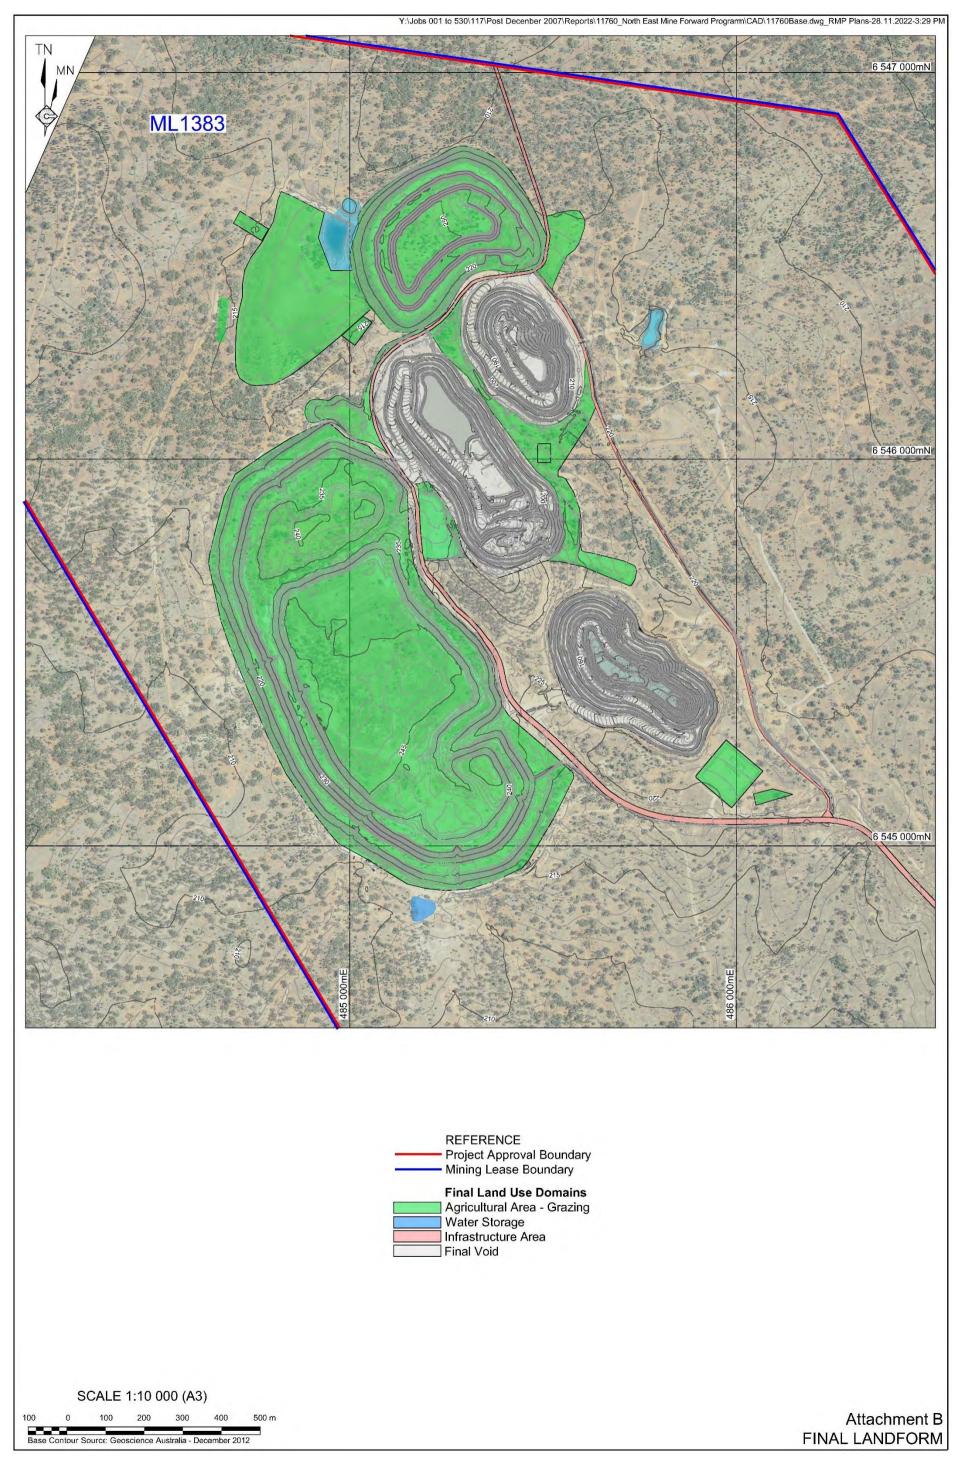

Attachment C

Rehabilitation Objectives and Rehabilitation Completion Criteria Table

(Total No. of pages including blank pages = 16)

Table B
Proposed Rehabilitation Objectives and Rehabilitation Completion Criteria

Page 1 of 15

Reference	Proposed Rehabilitation Objective	Indicator	Proposed Rehabilitation Completion Criteria	Page 1 of 1 Validation Method			
Final Land	Decommissioning Phase						
Use Domain Infrastructure Area Mining	All infrastructure and services not required for the final land use are removed.	Presence of services Presence of infrastructure	All relevant services disconnected. All relevant infrastructure removed.	Single occurrence relinquishment inspection and report, including photographs, following decommissioning (unless follow up actions are identified).			
Domain Infrastructure Area Spatial	Domain is free from hazardous materials and contaminants.	Presence of contaminated land	Contaminated land identified and remediated. Assessment indicates contamination within established NEPM criteria (applicable to final land use).	Contamination report prepared by qualified person following decommissioning with follow up validation testing, as required.			
Reference ¹		Presence of hazardous materials.	All hazardous materials removed.	Assessment, identification and removal of hazardous materials (such as asbestos, radiation devices, chemicals etc). Documented report by suitably qualified person verifying all materials removed.			
	4	Presence of waste	All rubbish and waste materials are removed from site or disposed of in areas designated in this plan.	Single occurrence relinquishment inspection and report, including photographs, following decommissioning (unless follow up actions are identified).			
				Waste tracking documentation for required waste streams removed from site.			
	Landform Establishmen	Landform Establishment Phase					
	Roads/tracks to be retained for a lawful final	Retained access road is in suitable condition.	Roads not required for final land use rehabilitated unless specified to be retained.	Single occurrence relinquishment inspection and report, including photographs and post closure plans			
	land use reduced in width / size to that suitable for final land use.		Road to be retained are reduced to 4m width suitable for final land use.				
	Free draining, stable and permanent landform established and suitable	Visual evidence of erosion.	Erosion within the landscape is not limiting final land use. Erosion does not exceed the natural erosion	Visual inspections undertaken and documented on a quarterly basis until site relinquishment. Records of any required corrective actions undertaken.			
	for a lawful final land use.		rate.	Visual inspections undertaken following significant rainfall events (i.e. ≥25mm of rainfall within 24 hours).			
	Rehabilitation Completic	Rehabilitation Completion / Relinquishment Phase					
	Relinquish lease and return of rehabilitation security.	Demonstrated compliance with all performance indicators.	Demonstrated compliance with all completion criteria.	Relinquishment report prepared by suitably qualified or experienced person(s).			

Page 2 of 15

Reference	Proposed Rehabilitation Objective	Indicator	Proposed Rehabilitation Completion Criteria	Page 2 of 18 Validation Method			
Final Land	Decommissioning Phase	Decommissioning Phase					
Use Domain Water Storage Area Mining	All infrastructure not suitable for lawful final land use will be removed.	Presence of infrastructure	All infrastructure not required for final land use to be removed.	Single occurrence relinquishment inspection and report, including photographs, following decommissioning (unless follow up actions are identified).			
Domain Infrastructure Area, Water Management	Contamination is not limiting final land use.	Presence of contaminated land.	Contaminated land identified and remediated. Assessment indicates contamination within established NEPM criteria (applicable to final land use).	Contamination report prepared by qualified person with follow up validation testing as required.			
Area – Clean Water, Water	Landform Establishmen	t Phase					
Management Area – Contaminated Water	Retained water management structures are stable and permanent overflow drainage is constructed.	Presence of suitable water management structures.	Water management structures are capable of retaining and conveying water without causing pollution.	Single occurrence relinquishment inspection and report, including photographs, following decommissioning (unless follow up actions are identified).			
Spatial Reference ¹ G3		Maintenance requirements (cost and frequency of works)	After 5 years maintenance levels for retained water management structures are commensurate with maintenance requirements for farm dams.	Review of dam maintenance recorded in annual reporting and comparison against local farm dam maintenance requirements (determined through interview with local landholders).			
	Retained water management structures are not a source of pollution.	Domain is non- polluting	Monitoring of water discharged from the Mine Site indicates that water quality is suitable for final land use through compliance with the ANZECC (2000) trigger values for slightly-moderately disturbed ecosystems or is consistent with ambient water quality.	Water quality testing, as per the <i>Water Management Plan 2016</i> , occurring monthly during and immediately following operations with frequency to be reduced progressively post-closure. Comparison (and documentation) of results against completion criteria			
	Rehabilitation Completion	on / Relinquishment Pl	hase				
	Relinquish lease and return of rehabilitation security.	Demonstrated compliance with all performance indicators.	Demonstrated compliance with all completion criteria.	Relinquishment report prepared by suitably qualified or experienced person(s).			

Page 3 of 15

Reference	Proposed Rehabilitation Objective	Indicator	Proposed Rehabilitation Completion Criteria	Validation Method		
Final Land	Decommissioning Phas	е				
Use Domain Final Void Area Mining Domain	All infrastructure not suitable for lawful final land use will be removed.	Presence of infrastructure	All infrastructure not required for final land use to be removed.	Single occurrence relinquishment inspection and report, including photographs, following decommissioning (unless follow up actions are identified).		
Void Spatial Reference ¹		Presence of waste	All rubbish and waste materials are removed from site or disposed of in areas designated in this plan.	Single occurrence relinquishment inspection and report, including photographs, following decommissioning (unless follow up actions are identified).		
J5	Landform Establishment Phase					
	Stable and permanent landform established.	Geotechnical stability of terminal benches/pit walls	Geotechnical assessment, by suitability qualified geotechnical engineer, based on site specific review, determines that the retained slopes are not likely to actively erode or 'slip' to an extent requiring further earthworks and profiling.	Single occurrence geotechnical review / report plan(s) prepared by surveyor and photographs included in relinquishment report, following completion of final landform establishment (unless further earthworks required).		
	Safe landform established.	Access to open cut and portal	Access to open cut, portal and decline sealed.	Single occurrence relinquishment inspection and report, including photographs, following decommissioning (unless follow up actions are identified).		
		Presence of safety bunds and fencing	Final void perimeter safety bund and fencing constructed to provide appropriate exclusion of access.	Visual inspection completed by site personnel, as part of regular site operation. Single occurrence relinquishment inspection and		
	Minimisation of final void catchments.	Presence of water management infrastructure	Final void perimeter safety bund and other water diversion structures constructed to minimise the catchment entering the void.	report, including photographs, following decommissioning (unless follow up actions are identified).		

Page 4 of 15

	B I B. I L 199	I	Book and Bolton British Britis	Page 4 of 15			
Reference	Proposed Rehabilitation Objective	Indicator	Proposed Rehabilitation Completion Criteria	Validation Method			
Final Land Use Domain Final Void Area	Non-polluting landform established.	Residual void does not risk serious environmental harm to land, surface waters	Safety bunding of the final void limits ingress of clean water to the void.	Visual inspection completed by site personnel, as part of regular site operation. Single occurrence relinquishment inspection and report, including photographs, following			
Mining Domain		groundwater, other than the		decommissioning (unless follow up actions are identified).			
Void Spatial Reference ¹ J5		environmental harm constituted by the existence of the residual void itself.	Final Void water balance and groundwater modelling conducted by suitably qualified person(s) verify the final void will be a groundwater sink.	Modelling report prepared by suitably qualified person(s) prior to completion of mining.			
			Surrounding landholders ability to use groundwater resources is not compromised.	Monthly water quality testing, as per the <i>Water Management Plan 2016</i> , during and immediately following operations with frequency to be reduced progressively post-closure.			
	Rehabilitation Completion	abilitation Completion / Relinquishment Phase					
	Relinquish lease and return of rehabilitation security.	Demonstrated compliance with all performance indicators.	Demonstrated compliance with all completion criteria.	Relinquishment report prepared by suitably qualified or experienced person(s).			
Final Land	Decommissioning Phas	е					
Use Domain Native Ecosystems – Grassland	All infrastructure not suitable for lawful final land use will be removed.	Presence of infrastructure.	All exposed pipework and infrastructure removed, where it is safe to do so.	Single occurrence relinquishment inspection and report, including photographs, following decommissioning (unless follow up actions are identified).			
Mining Domain	Contamination is not limiting final land use.	Presence of waste	All rubbish and waste materials are removed from site or disposed of in areas designated	Single occurrence relinquishment inspection and report, including photographs, following			
Heap Leach Pads			within this Plan.	decommissioning (unless follow up actions are identified).			
(referenced as Tailings Storage Facility in the portal)		Presence of contaminated land	Contaminated land assessment indicates landform is acceptable for final land use.	Contamination report prepared by qualified person with follow up validation testing as required.			
Spatial Reference ¹							
A2							

Page 5 of 15

Reference	Proposed Rehabilitation Objective	Indicator	Proposed Rehabilitation Completion Criteria	Validation Method
Final Land Use Domain Native Ecosystems – Grassland Mining	Contamination is not limiting final land use. (Cont'd)	Contamination of groundwater is contained or remediated.	Known groundwater contamination in the vicinity of the Heap Leach Pads is contained within the mining lease ML1280. Groundwater quality is consistent with criteria levels established in the <i>Water Management Plan 2016</i> , or is consistent with ambient water quality.	Water quality testing, as per the <i>Water Management Plan 2016</i> , occurring monthly during and immediately following operations with frequency to be reduced progressively post-closure. Groundwater contamination report prepared by qualified person.
Domain Heap Leach	Landform Establishmen	t Phase	damid.	
Pads (referenced as Tailings	Free-draining, stable and non-polluting landform established.	Presence of domestic grazing animals or pest species	Domestic grazing animals are excluded from the rehabilitation areas via protective fencing	Annual pest species inspection report (and subsequent control program, if required) included in annual rehabilitation revegetation reporting.
Storage Facility in the portal) Spatial Reference ¹ A2		Landform suitable for growth media establishment.	Landform to be constructed to the following specifications. Heap Leach Pad final landform to be no greater than approximately 20m in height. Drainage network to be constructed in accordance with surface water design specifications.	Landform as presented in as constructed 'as built' survey plans is consistent with engineering design specifications and surface water drainage plans. Geotechnical report of final landform indicates adequate stability to achieve final land use. Inspection and testing report, including photographs, prepared by a qualified person during and following landform construction.
		Construction of overlying store and release cover of Heap Leach Pads with appropriate geochemical and geotechnical composition of surface materials for final land use.	Heap Leach Pads are capped in accordance with engineered design specifications ¹ including a minimum 400mm covering of NAF waste rock or other suitable material.	Landform as presented in as constructed 'as built' survey plans is consistent with engineering design specifications. Geotechnical report and geochemical characterisation of capping material indicate adequate composition to achieve final land use. Inspection and testing report, including photographs, prepared by a qualified person during and following landform construction.

¹ See O'Kane Consulting, 2018. Murrawombie HLF Cover System and Landform Design. Prepared for Aeris Resources 28 August 2018.

Table B (Cont'd) Rehabilitation Objectives and Completion Criteria

Page 6 of 15

Reference	Proposed Rehabilitation Objective	Indicator	Proposed Rehabilitation Completion Criteria	Page 6 of 7 Validation Method
Final Land Use Domain Native Ecosystems –	5,	on-polluting landform polluting. Heap stablished. (Cont'd) water	Surface water (rainfall runoff) captured on the Heap Leach Pad surface is captured in a water management structure and diverted to the Open Cut Void.	Landform as presented in 'as constructed' survey plans is consistent with engineering surface water design and specifications. Inspection and testing report, including photographs,
Grassland Mining Domain			An engineered drain with a 1 in 100 year ARI capacity would be used to direct surface water to the Open Cut Void in accordance with surface water designs ¹ .	prepared by a qualified person during and following landform construction.
Heap Leach Pads (referenced as			No pooling of water on upper surface of the Heap Leach Pad facility is observed.	
Tailings Storage Facility in the			Contour/catch banks and drop-down water diversion structures are constructed at locations and as specified in engineering	Landform as presented in as constructed survey plans is consistent with engineering surface water design and specifications.
portal) Spatial			design plans and specifications ¹ .	Inspection (document) and repair (record) of any corrective actions to repair erosion.
Reference ¹	Growth Medium Develo	oment Phase		
A2	Establish soil / growing medium suitable for	Growth medium depth	Minimum growth medium depth of 100mm spread over domain.	Photographs included in a relinquishment report following growth medium spreading.
	grassland establishment.	Key soil characteristics	Analysis of growth medium indicates suitability for optimum vegetation growth of target communities including: ² .	Soil testing program and report, undertaken every year (or as specified by soil scientist) as part of regular rehabilitation monitoring and reporting, until
			pH between 5.6 and 7.3	revegetation criteria achieved.
		Organic matter levels at 4.5%		
			Available Phosphorous is 50mg/kg	
			Or, analysis of representative soil samples indicates these parameter are within 20% of analogue sites.	

_

² Primary performance indicators have been established through previous rehabilitation monitoring and sampling at analogue sites. See DnA Environmental 2020 Rehabilitation Monitoring Report. Secondary performance indicators are monitored to inform remediation requirements.

Table B (Cont'd) **Rehabilitation Objectives and Completion Criteria**

Deference	Proposed Rehabilitation	la dia stan	Proposed Rehabilitation Completion	Page 7 of 7
Reference	Objective	Indicator	Criteria	Validation Method
Final Land	Ecosystem and Land Us	se Establishment and L	Development Phase	
Use Domain Native Ecosystems – Grassland Mining Domain	Successful revegetation with suitable groundcover species.	Vegetation dominated by shallow rooted grassland species	Revegetation monitoring reports confirm that the mix of species spread/planted in revegetated areas can provide a minimum of 50% perennial ground cover and is capable of supporting the store and release cover system	Monitoring of revegetation success will involve a combination of quarterly visual assessments of plant establishment, groundcover and erosion by site personnel. Rehabilitation monitoring and reporting prepared by a suitably qualified person on rehabilitation condition,
Heap Leach Pads (referenced as		Vegetation is self- sustaining	Revegetation monitoring reports confirm that revegetated areas achieve the following vegetation community characteristics ³ .	with results reported on in the Annual Rehabilitation Report, every year and for a minimum of 5 years post-closure or otherwise until site relinquishment.
Tailings Storage Facility in the portal) Spatial			Landscape function analysis indices for landscape organisation, stability, infiltration and nutrient recycling are within 25% of analogue grassland sites or consistently trending towards them.	
Reference ¹ A2			Perennial plant cover is at a minimum of 50% to support store and release function of landform cover.	
			The presence of reproductive structures provides evidence that the ecosystem is maturing, capable of recruitment and is self-sustaining	
		Presence of weeds	Foliage cover of non-native and non-target species (weeds) is no greater than the surrounding vegetation / grassland analogue sites not disturbed by mining activities or impacting rehabilitated area.	Biannual weed inspection report (and subsequent control program, if required) included in annual rehabilitation revegetation reporting.

³ Primary performance indicators have been established through previous rehabilitation monitoring and sampling at analogue sites. See DnA Environmental 2020 Rehabilitation Monitoring Report. Secondary performance indicators are monitored to inform remediation requirements.

Page 8 of 15

	1			Page 8 of 1s
Reference	Proposed Rehabilitation Objective	Indicator	Proposed Rehabilitation Completion Criteria	Validation Method
Final Land	Ecosystem and Land Us	se Establishment and D	Development Phase	
Use Domain Native Ecosystems – Grassland	Successful revegetation with suitable groundcover species. (Cont'd)	Presence of domestic grazing animals or pest species	Access by domestic grazing animals is limited to ensure only controlled grazing may occur in rehabilitated area.	Annual pest species inspection report (and subsequent control program, if required) included in annual rehabilitation revegetation reporting.
Mining Domain			Feral and native animal control programs implemented. Pest species actively managed in consultation with neighbours.	
Heap Leach	Rehabilitation Completion	on / Relinquishment Ph	nase	
Pads (referenced as Tailings Storage Facility in the portal)	Relinquish lease and return of rehabilitation security.	Demonstrated compliance with all performance indicators.	Demonstrated compliance with all completion criteria.	Relinquishment report prepared by suitably qualified or experienced person(s).
Spatial Reference ¹				
A2			0 1	
Final Land Use Domain	Decommissioning Phas			
Native Ecosystems – Woodland	All infrastructure not suitable for lawful final land use will be removed.	Presence of infrastructure.	All infrastructure removed, where it is safe to do so.	Single occurrence relinquishment inspection and report, including photographs, following decommissioning (unless follow up actions are identified).
Mining Domain Waste Rock	Contamination is not limiting final land use.	Presence of waste	All rubbish and waste materials are removed from site or disposed of in areas designated within this plan.	Single occurrence relinquishment inspection and report, including photographs, following decommissioning.
Emplacement Spatial Reference ¹ A4		Presence of contaminated land	Contaminated land identified and remediated. Assessment indicates contamination within established NEPM criteria (applicable to final land use).	Contamination report prepared by qualified person with follow up validation testing as required.

Page 9 of 15

Reference	Proposed Rehabilitation Objective	Indicator	Proposed Rehabilitation Completion Criteria	Validation Method
Final Land	Landform Establishmen	t Phase		
Use Domain Native Ecosystems –	Appropriate geochemical, geotechnical composition of surface materials for	Waste Rock Emplacement is constructed of suitable	Geotechnical and geochemical characterisation, and (growth zone) soil sampling of surface material indicates	Geotechnical, geochemical characterisation and soil analysis report verifies that there are no impediments for achieving the final land use.
Woodland Mining Domain	final land use.	material to achieve the final land use.	adequate composition, fertility and parameters to achieve final land use.	Inspection and testing report, including photographs, prepared by a qualified person during and following landform construction.
Waste Rock Emplacement				Relinquishment inspection and report, including photographs upon closure.
Spatial Reference ¹	Free-draining, stable and non-polluting landform	Landform suitable for growth media	Waste Rock Emplacement constructed with three tiers each with a 10m vertical height.	Landform as presented in as constructed survey plans is consistent with engineering design
A4	established.	establishment.	Waste Rock Emplacement would remain stable post-closure.	specifications and surface drainage plan. Landform evolution modelling of final landform.
		Suitable erosion and sediment controls are installed and operating	No pooling of water on upper surface of the Waste Rock Emplacement is observed. Contour/catch banks and drop-down water	Geotechnical report of final landform indicates adequate composition and stability to achieve final land use.
		effectively.	diversion structures are constructed at locations and as specified in engineering design specifications.	Inspection and testing report, including photographs, prepared by a qualified person during and following landform construction.
				Relinquishment inspection and report, including photographs upon closure.

Table B (Cont'd) Rehabilitation Objectives and Completion Criteria

Page 10 of 15

Reference	Proposed Rehabilitation Objective	Indicator	Proposed Rehabilitation Completion Criteria	Page 10 of 1 Validation Method
Final Land	Growth Medium Develo	oment Phase		
Use Domain Native	Establish soil / growing medium suitable for	Compacted surfaces	Compacted surfaces deep ripped along contour.	Photographs included in a relinquishment report following deep ripping.
Ecosystems – Woodland	woodland establishment.	Growth medium depth	Minimum growth medium depth of 100mm spread over domain.	Photographs included in a relinquishment report following growth medium spreading.
Mining Domain Waste Rock Emplacement Spatial Reference ¹		Key soil characteristics	Analysis of growth medium indicates suitability for optimum vegetation growth of target communities according to recommended agricultural guidelines including ⁴ . • pH between 5.6 and 7.3	Soil testing program and report, undertaken every year (or as specified by soil scientist) as part of regular rehabilitation monitoring and reporting, until criteria achieved.
A4			 Organic matter levels at 4.5% Available Phosphorous is 50mg/kg Or, analysis of representative soil samples indicates these parameter are within 20% of analogue sites. 	
	Ecosystem and Land Us	se Establishment and D	Development Phase	
	Establishment of vegetation communities with a similar species composition to the surrounding native vegetation communities.	Revegetation species mix applied in accordance with species listed in Table 15 .	Revegetation monitoring reports confirm that revegetated areas achieve the following vegetation community characteristics ⁵ . • Landscape function analysis indices for stability and landscape organisation are within 25% of the woodland analogue sites or are trending in that direction • Diversity of species is within 25% of woodland analogue sites. • The composition of species comprising the vegetation community is within 25% of analogue sites (ecosystem composition). • The density of species is within 25% of the woodland analogue sites.	Monitoring of revegetation success will involve a combination of quarterly visual assessments of plant establishment, groundcover and erosion by site personnel. Rehabilitation monitoring reporting prepared by a suitably qualified person on rehabilitation condition, with results reported on in the Annual Rehabilitation Monitoring Report, every year and for a minimum of 5 years post-closure or otherwise until site relinquishment.

-

⁴ Primary performance indicators have been established through previous rehabilitation monitoring and sampling at analogue sites. See DnA Environmental 2020 Rehabilitation Monitoring Report. Secondary performance indicators are monitored to inform remediation requirements.

Table B (Cont'd)
Rehabilitation Objectives and Completion Criteria

Page 11 of 15

				Page 11 of 1	
Reference	Proposed Rehabilitation Objective	Indicator	Proposed Rehabilitation Completion Criteria	Validation Method	
Final Land Use Domain	vegetation communities with a similar species composition to the surrounding native vegetation communities (Cont'd) e Rock acement al	Vegetation is self- sustaining	Revegetation monitoring reports confirm that revegetated areas achieve the following		
Native Ecosystems – Woodland		vegetation community char expected from the surrounding native vegetation communities. (Cont'd) Landscape function and infiltration and nutrient recording in that direction Perennial plant cover, to and groundcover divers of the woodland analog. Vegetation structure, control the woodland analog. Vegetation structure, control the woodland analog. The presence of reproding such as buds, flowers of evidence that the ecosy capable of recruitment as	 vegetation community characteristics⁵. Landscape function analysis indices for infiltration and nutrient recycling are within 		
Mining Domain			25% of the woodland analogue sites or trending in that direction.		
Waste Rock Emplacement			Perennial plant cover, total groundcover and groundcover diversity are within 25% of the woodland analogue sites		
Spatial Reference ¹ A4					
			The presence of reproductive structures such as buds, flowers or fruit provides evidence that the ecosystem is maturing, capable of recruitment and can provide habitat resources comparable to the local		
		Presence of weeds	Rehabilitation monitoring of rehabilitation area confirms the diversity and foliage cover of non-native and non-target species (weeds) is equivalent to or less than surrounding vegetation / analogue sites not disturbed by mining activities or impacting rehabilitated area.	Biannual weed inspection report (and subsequent control program, if required) included in annual rehabilitation revegetation reporting.	

_

⁵ Primary performance indicators have been established through previous rehabilitation monitoring and sampling at analogue sites. See DnA Environmental 2020 Rehabilitation Monitoring Report. Secondary performance indicators are monitored to inform remediation requirements. See section XXXX for more information.

Page 12 of 15

Reference	Proposed Rehabilitation Objective	Indicator	Proposed Rehabilitation Completion Criteria	Validation Method	
Final Land Use Domain Native Ecosystems – Woodland Mining Domain Waste Rock Emplacement Spatial	Establishment of vegetation communities with a similar species composition to the surrounding native vegetation communities. (Cont'd)	Presence of domestic grazing animals or pest species	Domestic grazing animals are excluded from the rehabilitation areas via protective fencing. Feral and native animal control programs implemented in consultation with neighbours. Revegetation monitoring reports confirm grazing pressures are consistent with analogue sites not disturbed by mining. Monitoring confirms that, after 2 years pest species and abundance consistent with analogue sites.	Annual pest species inspection report (and subsequent control program, if required) included in annual rehabilitation revegetation reporting.	
Reference ¹	Rehabilitation Completic	on / Relinquishment Ph	nase		
A4	Relinquish lease and return of rehabilitation security.	Demonstrated compliance with all performance indicators.	Demonstrated compliance with all completion criteria.	Relinquishment report prepared by suitably qualified or experienced person(s).	
Final Land	Decommissioning Phas	е			
Use Domain Agricultural Area – Grazing Mining Domain Infrastructure Area, Water	All infrastructure not suitable for lawful final land use will be removed.	Any remaining infrastructure removed.	All infrastructure removed, where it is safe to do so.	Single occurrence relinquishment inspection and report, including photographs, following decommissioning (unless follow up actions are identified).	
	Contamination is not limiting final land use.	Presence of waste	All rubbish and waste materials are removed from site or disposed of in areas designated within this Plan.	Single occurrence relinquishment inspection and report, including photographs, following decommissioning.	
Management Area –		Presence of contaminated land	Contaminated land assessment indicates landform is acceptable for final land use.	Contamination report prepared by qualified person with follow up validation testing as required.	
Contaminated Water, Mine-	Landform Establishment Phase				
Related Disturbance, Topsoil Stockpile Area, Rehabilitation Area Spatial Reference ¹ B1, B3, B8a,	Free draining, stable and permanent landform established.	Drainage structures or dams.	Surface water and groundwater monitoring indicates that water quality is suitable for final land use through compliance with the ANZECC (2000) trigger values for slightly-moderately disturbed ecosystems or is consistent with ambient water quality.	Water quality testing, as per the <i>Water Management Plan 2016</i> , occurring monthly during and immediately following operations with frequency to be reduced progressively post-closure based on performance.	
B8b, B8c					

Table B (Cont'd) **Rehabilitation Objectives and Completion Criteria**

Page 13 of 15

	Proposed Rehabilitation		Proposed Rehabilitation Completion	Page 13 of		
Reference	Objective	Indicator	Criteria Renabilitation Completion	Validation Method		
Final Land Use Domain Agricultural Area – Grazing	Domain cultural - Grazing ng ain structure , Water agement - aminated er, Mine-	Drainage structures or dams. (Cont'd)	Decommissioned dams have been backfilled and landform constructed to blend with surrounding topography.	Single occurrence relinquishment inspection and report, including photographs, following decommissioning (unless follow up actions are identified).		
Mining Domain Infrastructure Area, Water Management Area – Contaminated Water, Mine- Related		Presence of stockpiled material	All stockpiled material removed or surface appropriately profiled.	Single occurrence relinquishment inspection and report, including photographs, following completion of final landform establishment (unless follow up actions are identified).		
		Construction of final landform.	Suitable erosion and sediment controls are installed and operating effectively.	Single occurrence relinquishment inspection and report, including photographs, following completion of final landform establishment (unless follow up actions are identified).		
Disturbance,	Growth Medium Development Phase					
Topsoil Stockpile Area, Rehabilitation Area Spatial Reference ¹ B1, B3, B8a, B8b, B8c	Establish soil / growing medium suitable for grassland establishment.	Compacted surfaces	Compacted surfaces deep ripped along contour.	Photographs included in a relinquishment report following deep ripping.		
		Growth medium depth	Minimum growth medium depth of 100mm spread over domain.	Photographs included in a relinquishment report following growth medium spreading.		
		Key soil characteristics		Photographs included in a relinquishment report following growth medium spreading annually until site relinquishment. Soil testing program and report, undertaken every		
				year (or as specified by soil scientist) as part of regular rehabilitation revegetation reporting, until criteria achieved.		
			pH between 5.6 and 7.3			
			Organic matter levels at 4.5%			
			Available Phosphorous is 50mg/kg			
			Or, analysis of representative soil samples indicates these parameter are within 20% of analogue sites.			

⁶ Primary performance indicators have been established through previous rehabilitation monitoring and sampling at analogue sites. See DnA Environmental 2020 Rehabilitation Monitoring Report. Secondary performance indicators are monitored to inform remediation requirements.

Table B (Cont'd) **Rehabilitation Objectives and Completion Criteria**

	Drawaged Bahabilitation Drawaged Bahabilitation Completion				
Reference	Proposed Rehabilitation Objective	Indicator	Proposed Rehabilitation Completion Criteria	Validation Method	
Final Land Use Domain Agricultural Area – Grazing Mining Domain Infrastructure Area, Water Management Area – Contaminated Water, Mine- Related Disturbance, Topsoil Stockpile Area, Rehabilitation Area Spatial Reference¹ B1, B3, B8a, B8b, B8c	Establishment of vegetation communities with a species composition conducive to grazing land use. Revegetation species mix applied in accordance with species listed in Table 15. Vegetation is self-sustaining	Revegetation species mix applied in accordance with species listed in Table 15.	Revegetation monitoring reports confirm that revegetated areas achieve the following vegetation community characteristics ⁷ . Landscape function analysis indices for stability and landscape organisation are within 25% of the woodland analogue sites or are trending in that direction Diversity of species is within 25% of woodland analogue sites. The composition of species comprising the vegetation community is within 25% of analogue sites (ecosystem composition). The density of species is within 25% of the woodland analogue sites. Revegetation monitoring reports confirm that	Monitoring of revegetation success will involve a combination of quarterly visual assessments of pla establishment, groundcover and erosion by site personnel. Rehabilitation monitoring reporting prepared by a suitably qualified person on rehabilitation condition with results reported on in the Annual Rehabilitation Monitoring Report, every year and for a minimum of years post-closure or otherwise until site relinquishment.	
		revegetated areas achieve the following vegetation community characteristics ⁷ . • Landscape function analysis indices for infiltration and nutrient recycling are within 25% of the woodland analogue sites or trending in that direction. • Perennial plant cover, total groundcover and groundcover diversity are within 25% of the woodland analogue sites • Vegetation structure, composition and tree density and diversity are within 25% of the woodland analogue sites • The presence of reproductive structures such as buds, flowers or fruit provides evidence that the ecosystem is maturing, capable of recruitment and can provide habitat resources comparable to the local remnant vegetation.			

⁷ Primary performance indicators have been established through previous rehabilitation monitoring and sampling at analogue sites. See DnA Environmental 2020 Rehabilitation Monitoring Report. Secondary performance indicators are monitored to inform remediation requirements.

Table B (Cont'd) Rehabilitation Objectives and Completion Criteria

Page 15 of 15

Reference	Proposed Rehabilitation Objective	Indicator	Proposed Rehabilitation Completion Criteria	Validation Method	
Final Land Use Domain Agricultural Area – Grazing Mining Domain	Domain cultural a – Grazing ing nain estructure a, Water agement a – taminated vegetation communities	Presence of weeds	Rehabilitation monitoring of rehabilitation area confirms the diversity and foliage cover of non-native and non-target species (weeds) is equivalent to or less than surrounding vegetation / analogue sites not disturbed by mining activities or impacting rehabilitated area.	Biannual weed inspection report (and subsequent control program, if required) included in annual rehabilitation revegetation reporting.	
Area, Water Management		Presence of domestic grazing animals or	Domestic grazing animals are excluded from the rehabilitation areas via protective fencing.	Annual pest species inspection report (and subsequent control program, if required) included in annual rehabilitation revegetation reporting.	
Area – Contaminated		pest species	Feral and native animal control programs implemented in consultation with neighbours.		
Water, Mine- Related Disturbance, Topsoil Stockpile Area, Rehabilitation Area		Revegetation monitoring reports confirm grazing pressures are consistent with analogue sites not disturbed by mining. Monitoring confirms that, after 2 years pest species and abundance consistent with analogue sites.			
Spatial Reference ¹	Land capability similar to pre-mining capability (Class V or Class VI).	Land capability	Land capability, assessed in accordance with OEH 2012, of Class V or Class VI.	Assessment report, included in relinquishment report, prepared by suitably qualified consultant.	
B1, B3, B8a, B8b, B8c		Agricultural productivity	Agricultural productivity trending towards analogue sites and consistent with Land Capability Class established in OEH, 2012.	Single occurrence production report, prepared a suitable independent person, post closure (unless further activities required).	
	Rehabilitation Completion / Relinquishment Phase				
	Relinquish lease and return of rehabilitation security.	Demonstrated compliance with all performance indicators.	Demonstrated compliance with all completion criteria.	Relinquishment report prepared by suitably qualified or experienced person(s).	
